Strategic Timeline March 2021 v1.14

Consultation Activity | Key Event/Milestone | Council Committees | Work Activity | Dependencies
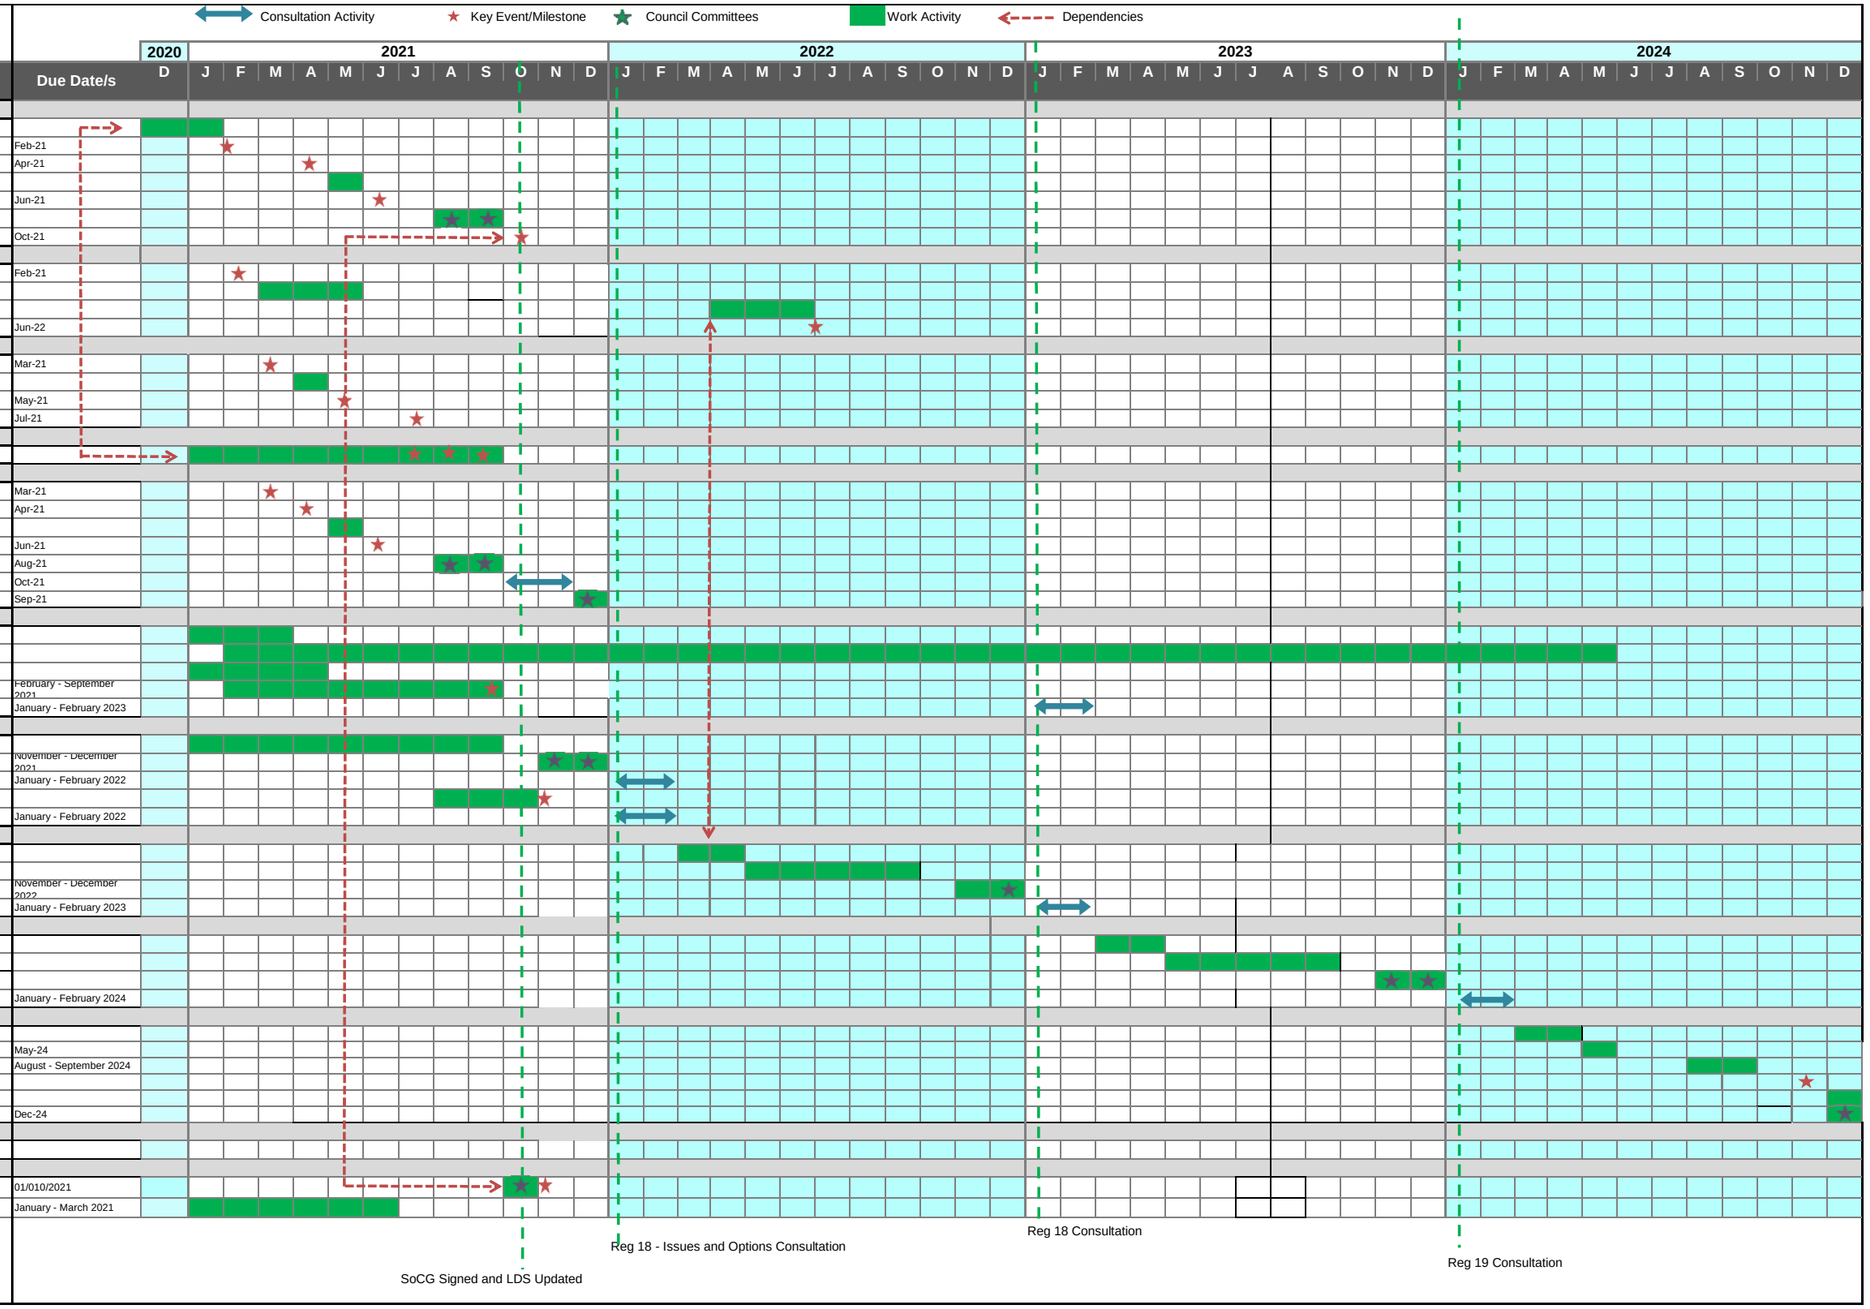
South West Herts JSP - Strategic Timeline	Due Date/s
STATEMENT OF COMMON GROUND (SoCG)	
Prepare first draft of SoCG	
Present first draft of SoCG to SPOG for comments	Feb-21
Present draft of SoCG to SG for comments	Apr-21
Revise and prepare final draft version of SoCG	
Present draft SoCG to SPMG for approval	Jun-21
Endorsement of SoCG by Councils	
SoCG signed by Councils	Oct-21
Strategic Growth Locations Study (SGLS) and Multi Modal Study (MMS)	
Receive draft Spatial Options - SPOG	Feb-21
SGLS and MMS - SPOG review of initial spatial options (Stage 2)	
Prepare Preferred Spatial Option (Stage 3)	
Receive Preferred Spatial Option (Stage 3)	Jun-22
Recruit 2 x JSP Officers	
Present first draft of JD to SPOG for comments	Mar-21
Advertise positions	
Appoint preferred candidates	May-21
Officers starts work	Jul-21
JSP PREPARATION	
Agree scope of JSP with SPOG, SG and SPMG	
STATEMENT OF COMMUNITY INVOLVEMENT (SCI)	
Present first draft of SCI to SPOG for comments	Mar-21
Present draft of SCI to SG for comments	Apr-21
Revise and prepare final draft version of SCI	
Present draft SCI to SPMG for approval	Jun-21
Endorsement of SCI by Councils	Aug-21
SCI Consultation	Oct-21
Adoption of SCI by Councils	Sep-21
JSP EVIDENCE PREPARATION	
Existing Evidence Audit to identify any gaps	
Instruct evidence to support JSP	
Procure Legal support to the programme	
JSP Visioning Exercise	February - September 2021
SW Wide Herts 'Call for Sites'	January - February 2023
Regulations 18 - Issues & Options (Vision and Objectives)	
Issues and Options Plan Preparation	
Endorsement by Partner Councils of Issues & Options JSP and SA/SEA Scope	November - December 2021
Consultation on Issues & Options JSP	January - February 2022
Preparation of SA/SEA scoping report	
SA/SEA scoping consultation	January - February 2022
Regulation 18 - Spatial Options and Preferred Option	
Review Issues & Options responses	
Agree draft spatial options (and preferred spatial option) for Preferred Options consultation	
Endorsement by Partner Councils of Reg 18/Spatial options and Preferred Option(s) JSP	November - December 2022
Consultation on Reg 18/Spatial options and preferred option and Policies JSP	January - February 2023
Regulation 19 - Publication Plan	
Review Preferred Option responses and update plan	
Prepare Publication Plan for Reg 19 consultation	
Endorsement by Councils of Reg 19/Publication JSP and SA/SEA (with delegation to submit to PINS)	
Consultation on Reg 19/Publication JSP and SA/SEA	January - February 2024
Examination in Public	
Review Reg 19 responses, update plan and prepare proposed Mods for submission with plan	
Submission of Draft JSP to PINs	May-24
Examination in Public of JSP	August - September 2024
PINs report on JSP	
Publication of proposed modifications	
Adoption of JSP by partner authorities	Dec-24
Other External Milestones	
Government White Paper	
Other programme deliverables	
Update District LDS's	01/010/2021
Prepare JSP Comms Plan and website	January - March 2021
